



PRINCE2 Course



Course Objectives

- ***Understanding the formal project management framework using PRINCE2***
- ***Understanding PRINCE2 Principles, Themes and Processes***
- ***Building confidence for facing PRINCE 2 Foundation and Practitioner Exams***

Course Agenda

Day 1

- **Introduction to Prince 2**
- **Overview of Prince 2 Principles, Themes and Processes**
- **Prince 2 Principles**
 - Continued Business Justification
 - Learn from Experience
 - Defined Roles & Responsibilities
 - Manage by stage
 - Manage by Exception
 - Focus on Product
 - Tailoring

Day 2

- **Prince 2 Themes**
 - Business Case
 - Organization

Day 3

- **Prince 2 Themes**
 - Quality
 - Plans

Course Agenda

Day 4

- **Prince 2 Themes**
 - Risk
 - Change
 - Progress

Day 5

- **Prince 2 Processes**
 - Starting up
 - Directing

Day 6

- **Prince 2 Processes**
 - Initiating
 - Controlling

Day 7

- **Prince 2 Processes**
 - Managing Product Delivery
 - Managing Product Boundary

Day 8

- **Prince 2 Processes**
 - Closing
 - Revision of Prince 2

What is PRINCE2?

PRINCE2 (an acronym for **P**Rojects **I**N a **C**ontrolled **E**nvironments) is a de facto process-based method for effective **project management**.

PRINCE2 can be tailored and applied to any project regardless of project scale, type, organization, geography or culture.

PRINCE2 Foundation & Practitioner Exams

Following two examinations applicable to PRINCE2:

-  Foundation examination
-  Practitioner examination

Foundation Examination Details

- The Foundation is the first of the two PRINCE2 Examinations you are required to pass to become a PRINCE2 Practitioner.



This is a basic level exam that aims to measure whether a candidate would be able to act as an informed member of a project management team using the PRINCE2 method within a project environment supporting PRINCE2.

The candidate should have good understanding of



Four Integrated Elements of Prince2 - Principles, Processes, Themes



and the Project Environment



Prince2 Project organization structure, key roles and the responsibilities

associated with the roles

Foundation Exam Format

Multiple-choice

One hour duration

75 questions

35 correct answers are required to pass

Closed-book

Practitioner Examination Details

- The Practitioner is the second of the two PRINCE2 Examinations you are required to pass to become a PRINCE2 Practitioner.
- This level aims to assess whether a candidate would be able to apply PRINCE2 to the real time project within an environment supporting PRINCE2. To demonstrate this candidate needs to exhibit the competence required for the Foundation qualification, and show that they can apply and tune PRINCE2 to address the needs and problems of a specific project.

Precisely the candidates must be able to:

- Produce detailed explanations of all processes, components and techniques, and worked examples of all PRINCE2 products as they might be applied to address the particular circumstances of a given project scenario.
- Show they understand the relationships between Principle, Themes, Processes and the PRINCE2 products and can apply this understanding
- Demonstrate their ability to tailor PRINCE2 to different project environments.

Practitioner Exam Format

- The Practitioner exam presents the following main characteristics:
- 9 questions, with a scenario background and appendices
Each of the 9 questions is worth 12 marks
- An overall score of 59 out of possible 108 is required to pass (55%)
- 2.5 hours duration
- **Open book examination (only the PRINCE2 Manual is allowed) This will be available to each delegate**

For Practitioners & Registered Practitioners

All PRINCE2 Practitioners should be re-registered within 5 years of their original certification. This Re-Registration comprises a 1-hour examination set at the same standard as the Practitioner examination.

History of PRINCE 2

PRINCE2 methodology was first established in 1989 by the British Government's CCTA (the Central Computer and Telecommunications Agency).

The method was originally based on PROMPT, a project management method created Simfact Systems Ltd in 1975. PROMPT was adopted by CCTA in 1979 as standard to be used for all government information system projects. When PRINCE2 was launched in 1989, it effectively superseded PROMPT within government projects.

2009 – major refresh to align with other terminology

2017 – Refreshed to describe more about tailoring
Currently PRINCE2 is a registered trademark of Cabinet Office (HM, Govt of UK) in the United Kingdom and other countries.

**De facto a standard for UK government
Used by public and private sector worldwide**

Project Management Basics

What is a Project?

PRINCE2 Definition

“A temporary organization that is created for the purpose of delivering one or more business Products according to an agreed Business Case”

Some of the other Project Management frameworks define project as:

“A temporary Endeavour undertaken to create a unique product,
service or result”

Some examples of the project are:

- Filming a Motion Picture
- Construction of a building – Office, Hospital or a shopping mall
- Moving the office from one building to another
- Hosting an event
- Creating a new process
- Creating a Product
- Developing a software
- Implementing a software product
- Major Enhancement to a Software

What makes a project a PRINCE 2 project

For a project to be following PRINCE 2, as a minimum it must be possible to demonstrate that the project:

- Is applying PRINCE 2's principles
- Is meeting the minimum requirements set out in the PRINCE 2 themes
- Has project processes that satisfy the purpose and objectives of the PRINCE 2 processes
- Is either using PRINCE 2's recommended techniques or using alternative, equivalent techniques

Characteristics of the project

They bring about Change. All the projects brings change, the change can be in the form of process, products, tools and techniques, organization structure or at the least expectations.

They are **temporary** (They have a defined **Start** and a defined **End**).


They are usually **Cross-functional**. Projects involve a team of people with different skills working together. Examples – Engineers, Testers, Business Analyst and so on.

Every Project is **Unique**. Though there may be common elements in the project but the two projects will differ in terms of the team, location and environment. Example constructing a shopping mall providing similar offerings in two different locations.

Characteristics of the project

- There is a degree of Uncertainty associated with all the projects
- Projects are progressively elaborated. A project starts with a vision or goal. The goal is converted into a high level plan and as you proceed forward the requirements unfold and you get more clarity on the requirements and this helps you to plan the immediate future at a detailed level.

The diagram below depicts High level view of a project life cycle (Single Phase)

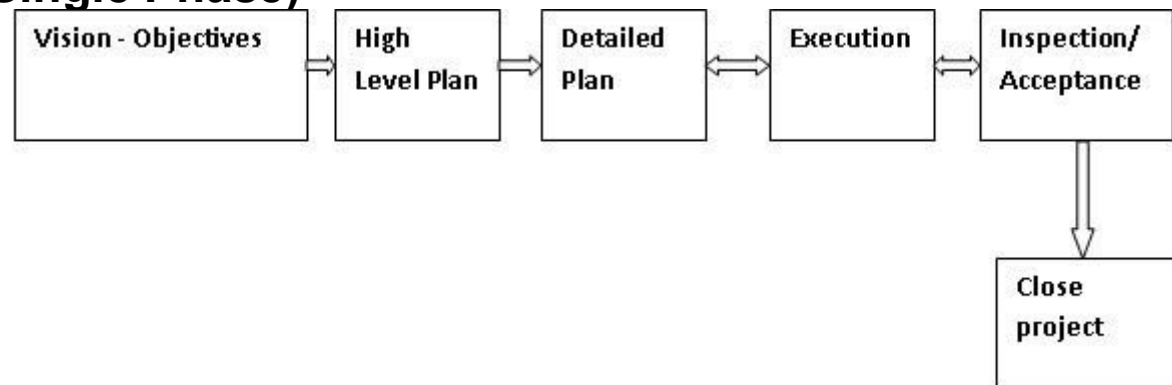

Project Vs Operations

PROJECTS	OPERATIONS
Temporary	Ongoing
Unique	Repetitive
Closes after attaining the objectives	Objective is to sustain business
Examples are : Launching the new car model	Examples are : Assembly line production, Monthly Payroll

What is project management

- Project Management is the application of knowledge, skills, tools and techniques to project activities to meet the project requirements.
- The project team carries out the work needed to complete the project, while the project manager schedules, monitors, and controls the various project tasks.
- The project manager requires **knowledge, performance, and personal** skills to perform better at their jobs.

The typical work of a project manager involves:

1. **Requirements gathering**
2. **Managing stakeholder expectations**
3. **Managing key projects Aspect** including scope, quality, schedule, resources, Benefits, and risk.

Six Aspects of Project

The 6 Aspects or variables / performance targets are :Timescales, Costs, Quality, Scope,Benefits and Risk

Timescales

Scope

Cost

Benefits

Quality

Risk

What is a Programme?

Author - Pankaj

What is a Programme?

A Project can run as a stand-alone entity or can be part of a programme of related projects.

A Programme is a temporary flexible organizational structure created to coordinated, direct and oversee the implementation of a set of related projects and activities in order to deliver outcomes and benefits related to organization's strategic objectives.

A programme is likely to have a longer life than a single project. A project which forms the part of a programme may be impacted by the programme structure and the reporting requirements.

Programme Management may be defined as the co-ordinated organisation, direction and implementation of a portfolio of projects and activities that together achieve outcomes and realise benefits that are of strategic importance."

PRINCE2 Integrated Environment

The PRINCE2 methodology is based on four integrated elements and these elements are **Principles, Themes, Processes** and the **Tailoring PRINCE2 to Project Environment** as depicted in the figure below



Embedding and Tailoring PRINCE2

Embedding	Tailoring
Done by the organization to adopt PRINCE2	Done by the project management team to adapt the method to the context of a specific project
Focus on: • Process responsibilities • Scaling rules / guidance • Standards (templates, definitions) • Training and development • Integration with business processes • Tools • Process assurance	Focus on: • Adapting the themes through the strategies and controls • Incorporating specific terms/ language • Revising the Product Descriptions for the management products • Revising the role descriptions for the PRINCE2 project roles • Adjusting the processes to match the above
Guidance in PRINCE2 method	Guidance in this pocket guide

PRINCIPLES

- **Continued Business Justification**
- **Learn from Experience**
- **Define Roles and Responsibilities**
- **Manage by Stages**
- **Manage by Exception**
- **Focus on Products**
- **Tailor to suit the project environment:**

Themes


-  **Business Case**
-  **Organization**
-  **Quality**
-  **Plans**
-  **Risks**
-  **Change**
-  **Progress**

Processes

The seven processes listed below describe the project lifecycle from getting started to project closure.


- Starting Up a Project
- Initiating a Project
- Controlling a Stage
- Managing Product Delivery
- Managing a Stage Boundary
- Directing a Project
- Closing a Project

PRINCIPLES , PROCESSES AND THEMES

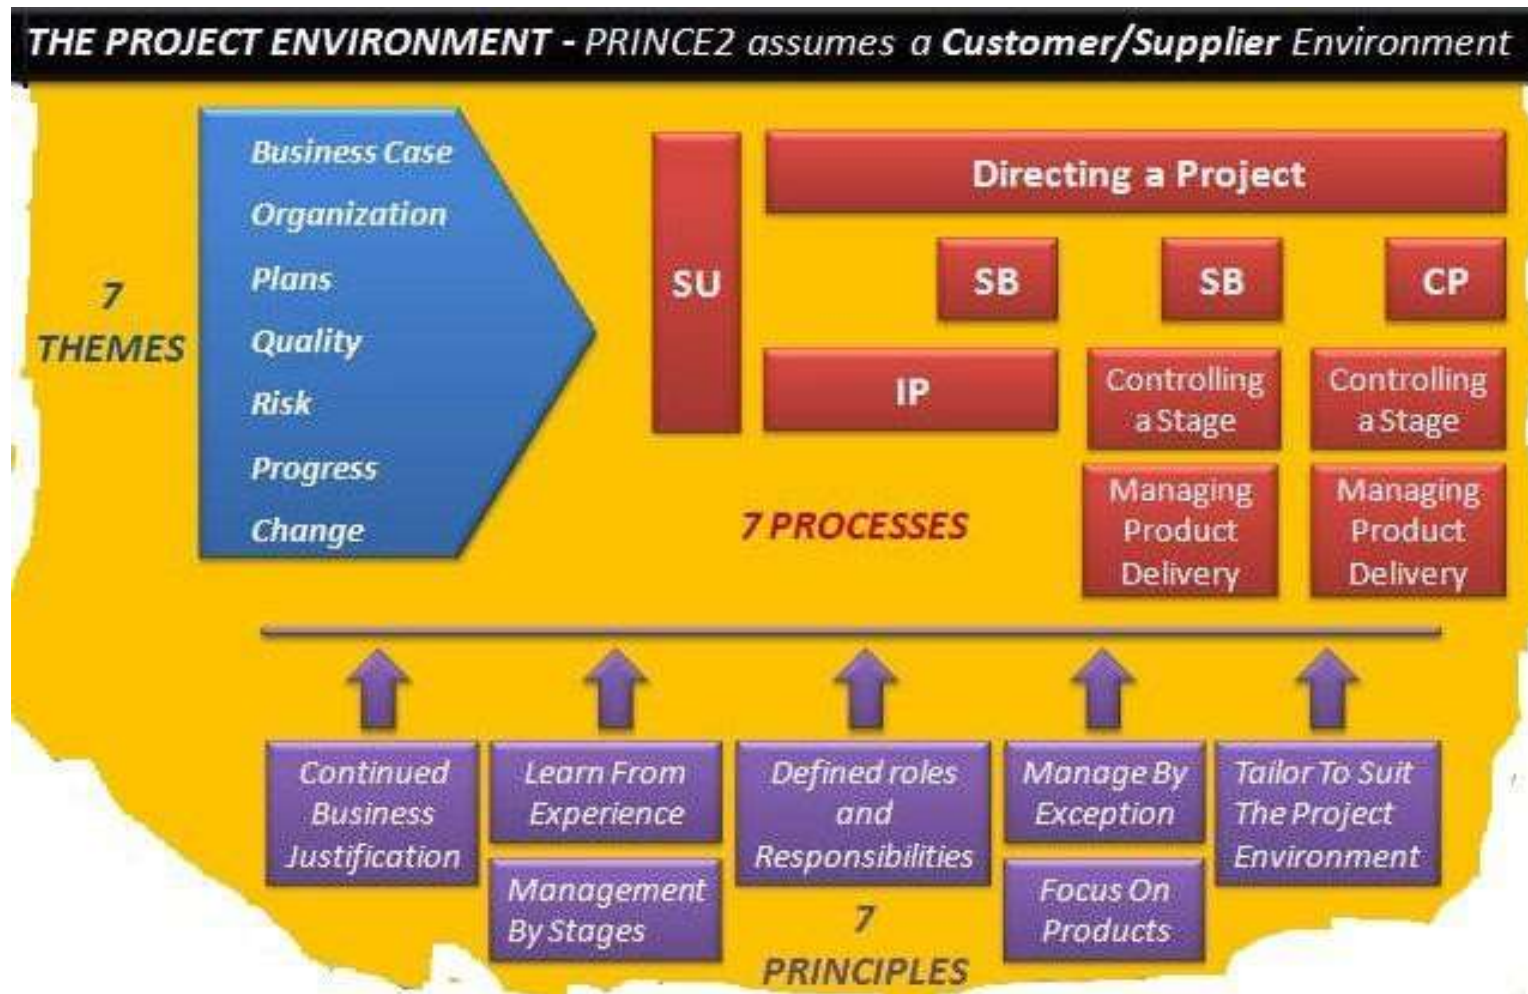

PRINCE2 PROCESS TIMELINE

The PRINCE2 Process Timeline

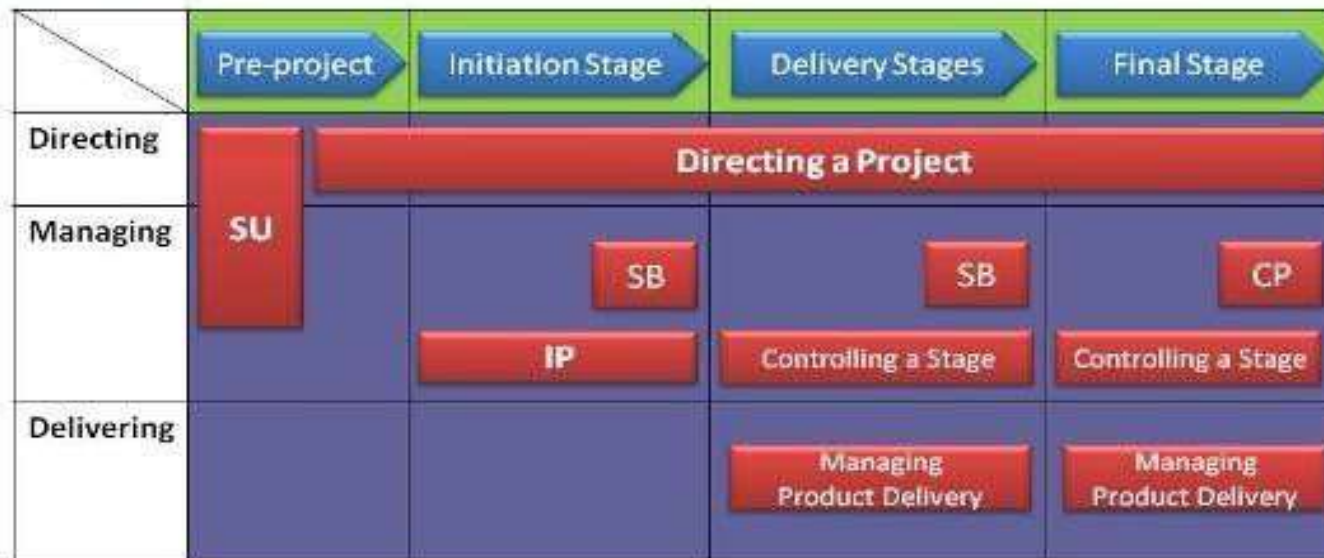

26 management products

Help you plan, manage and control the project


Most are created by the project manager:

BASELINES – define aspects of the project and once approved are subject to change control

RECORDS – dynamic management products that maintain information regarding project progress

REPORTS– provide a snapshot of the status of certain aspects of the project

Roles

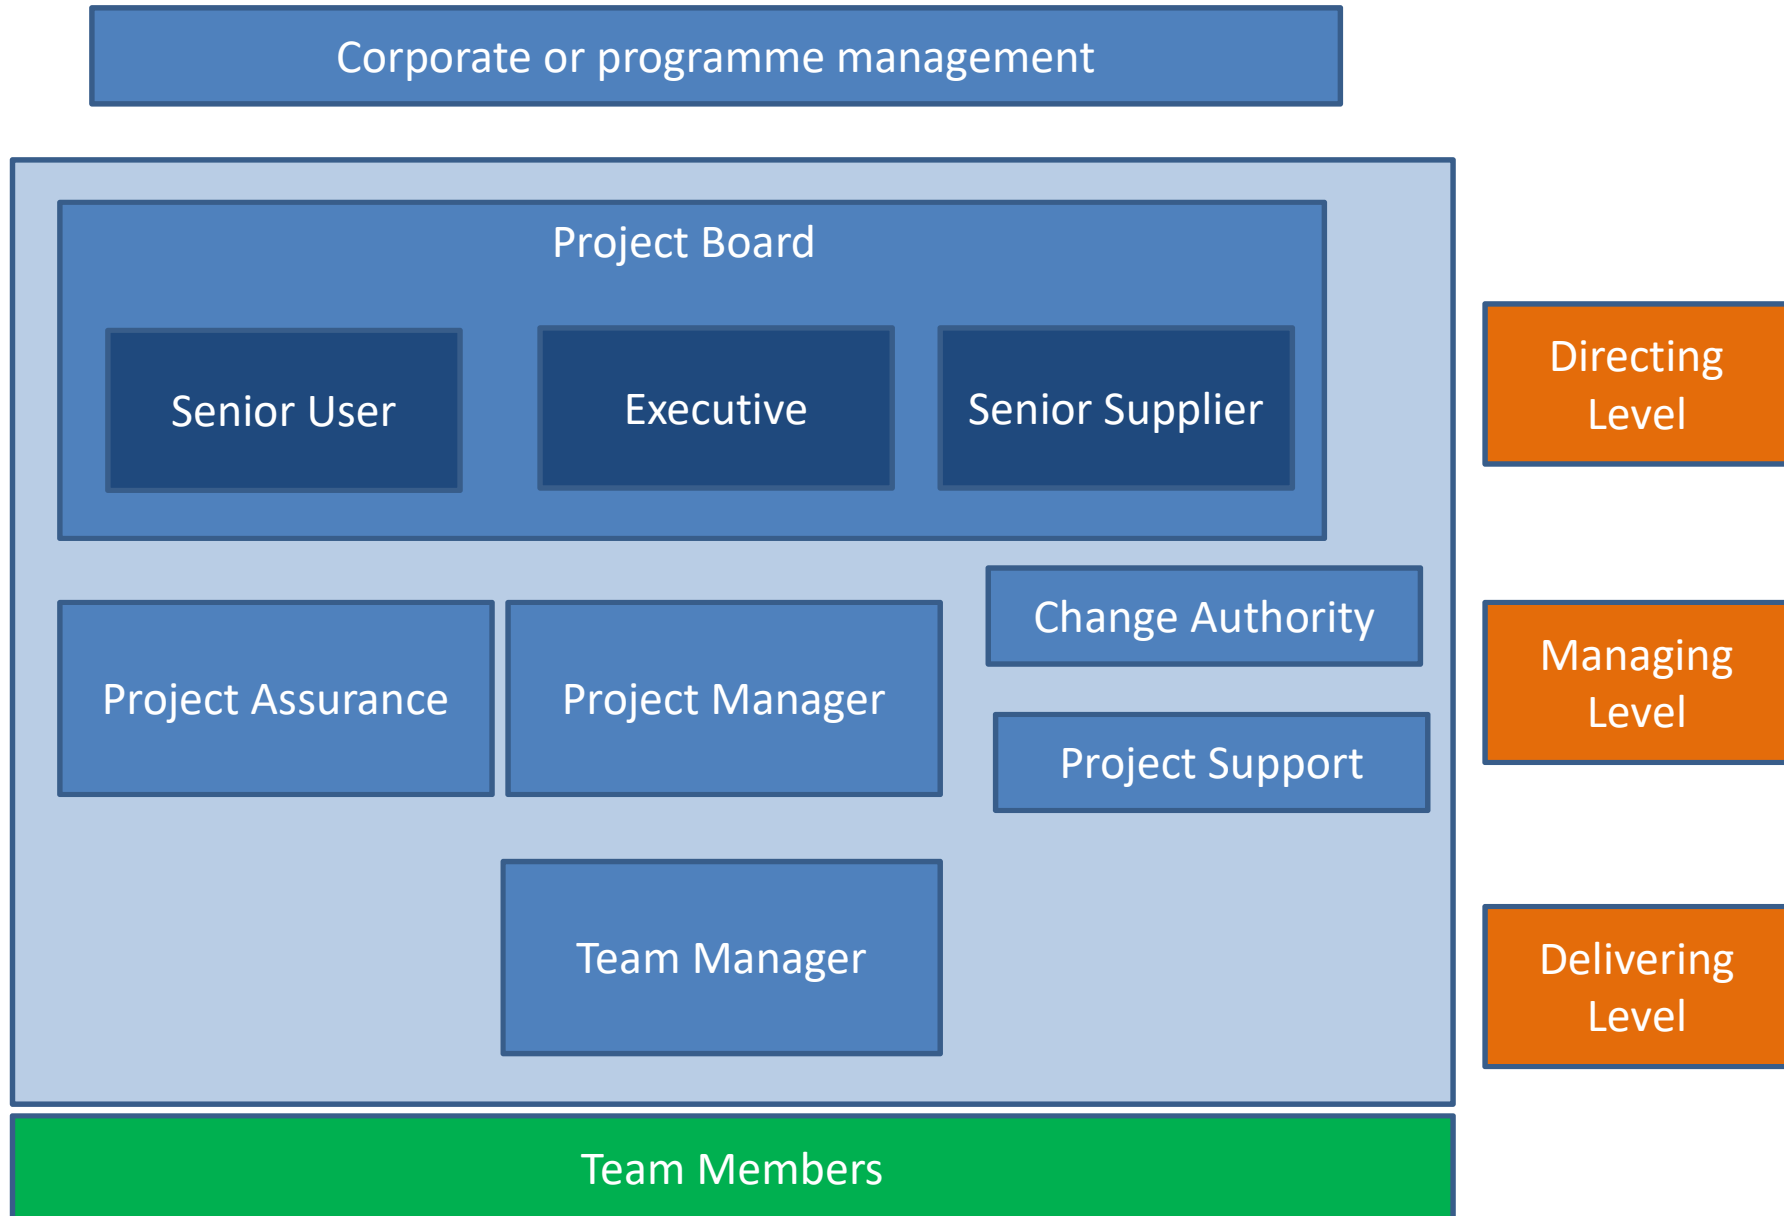

What PRINCE 2 does not provide

Specialist aspects

- Can work alongside specialist method (e.g. engineering, change management)
- PRINCE 2 describes “management products” required to manage, but “specialist products” need to be identified and included in the project’s scope and plans
- Detailed techniques
- Leadership capabilities

PRINCE2 Benefits

PRINCE2's formal recognition of responsibilities within a project, together with its focus on what a project is to deliver (the why, when and for whom) provides projects with:

- A common, consistent approach – based upon proven best practices and governance for managing projects

- A controlled and organized start, middle and end

- Regular reviews of progress against plan

- Assurance that the project continues to have a business justification

- Flexible decision points

- Management control of any deviations from the plan

PRINCE2 Benefits

- The involvement of management and stakeholders at the right time and place during the project
- Good communication channels between the project, project management, and the rest of the organisation
- A means of capturing and sharing lessons learned
- A route to increasing the project management skills and competences of the organisation's staff at all levels



PRINCIPLES

Principles

UNIVERSAL – to every project

SELF-VALIDATING – proven in practice

EMPOWERING - enable practitioners to influence how the project will be managed

Continued business justification

The justification is documented and approved

Even compulsory project requires documentation

There is a justifiable reason to start it

The justification should remain valid throughout the life of the project

Learn form experience

Lessons should be included in all reports and reviews

If the project is a “first” for the people within the organization, then they should learn from others by seeking external experience

Defined roles and responsibilities

All project have the following primary stakeholders

- Business - Sponsor who endorse the objectives and ensure the project gives value for money and delivers products which meet business needs
- Users – they will use the products to enable them to gain the intended benefits
- Suppliers – provide the “specialist” resources and expertise to deliver products
- The project board includes all 3 interests. In a customers/supplier environment the “customer” usually means a collective term for both the business and the user interests

Manage by stages

A project is planned, monitored and controlled stage-by-stage

Use at least 2 management stages, or more depending on the risks

Managements stages provide the project board with control points at major intervals

Only plan to a level of detail that is manageable and foreseeable

Manage by exception

An exception is a forecast to deviate BEYOND the agreed level of authority and must be referred up to the next management layer of decision.

Tolerances can be set for time, cost, quality, scope, benefits, risk. They define the limits of delegated authority and accountability.

Tolerances are set by corporate/programme management, the project board and by the project manager.

Unless a plan is forecast to deviate from its tolerances, the project board does not need to meet the project manager, and will receive regular highlight reports instead.

Management by exception is a very efficient use of senior management time.

Focus on products

2 types of products

- Management which the project manager creates
- Specialist which the team creates
- Use product-based planning when creating plans
- A successful project is output oriented not activity oriented
- Product description

Tailor to suit the project environment

Tailor PRINCE 2 to suit the project's size, complexity, importance, capability and risk

The purpose of tailoring is to ensure the project management method relates to the project's environment

You can tailor the themes, processes and management products
